

Shelter and Non Food Items Cluster

Settlement and Shelter Strategic Outlines


Outcomes of the Workshop

Kurdistan Region of Iraq

Erbil, August 2014

Planning Figures

Estimated 1,7 million displaced people in Iraq as of 27th August

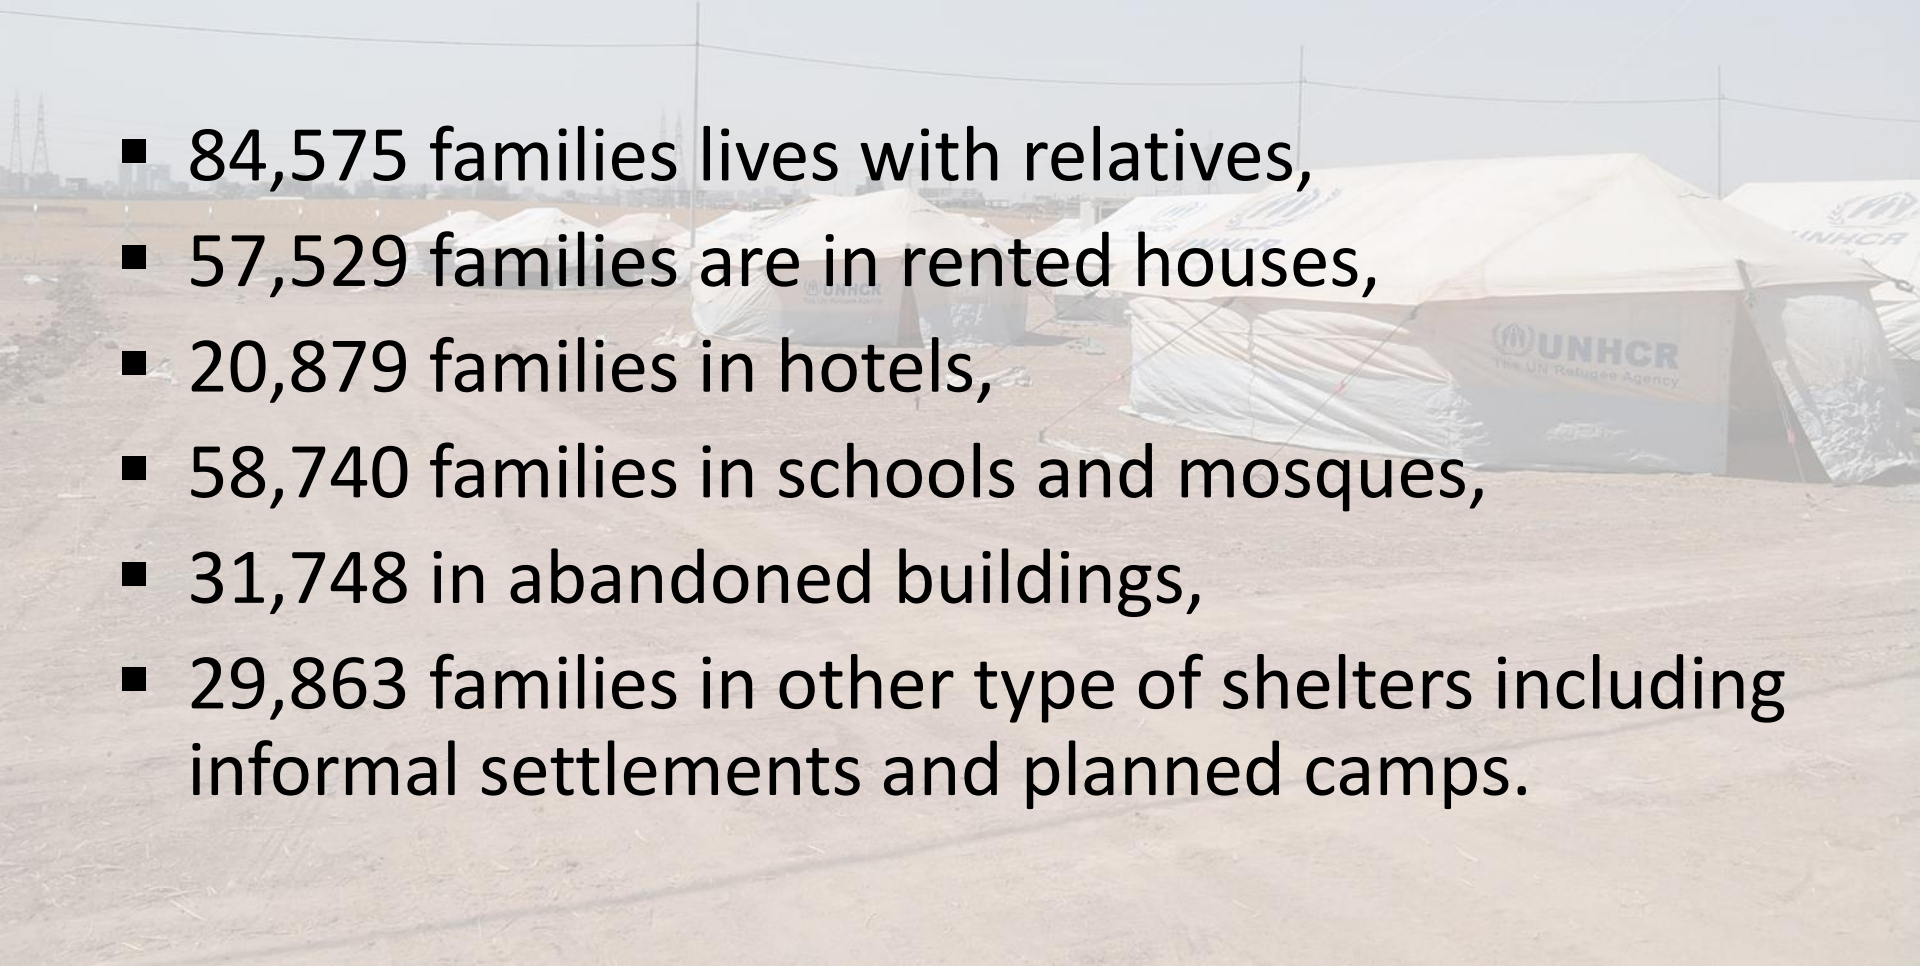- 84,575 families lives with relatives,
 - 57,529 families are in rented houses,
 - 20,879 families in hotels,
 - 58,740 families in schools and mosques,
 - 31,748 in abandoned buildings,
 - 29,863 families in other type of shelters including informal settlements and planned camps.
- 

It is estimated that out of 1.7 million
around **850,000 people**
are displaced in Kurdistan Region of Iraq

Targeting - Prioritization

- Families living in the open, squatting in parks.
- Families living in schools, mosques, churches
- IDPs residing in unfinished buildings in substandard living conditions and no proper access to services (e.g. sanitation)


Immediate Response

An initial **emergency shelter response (camps)** is provided by end of October to meet urgent shelter needs of IDPs living in open air and schools, mosques, churches.

Risk: possibility that not all schools will be vacated by end of October.

Winterisation

- Shelter solutions offer decent living conditions and protection from adverse climate conditions **by November**




Post emergency

In the next four/six months undertake camps consolidation to gradually evolve into more sustainable solutions while possible returns may take place.

Contingency

Develop a contingency plan to address shelter needs for possible new displacements.

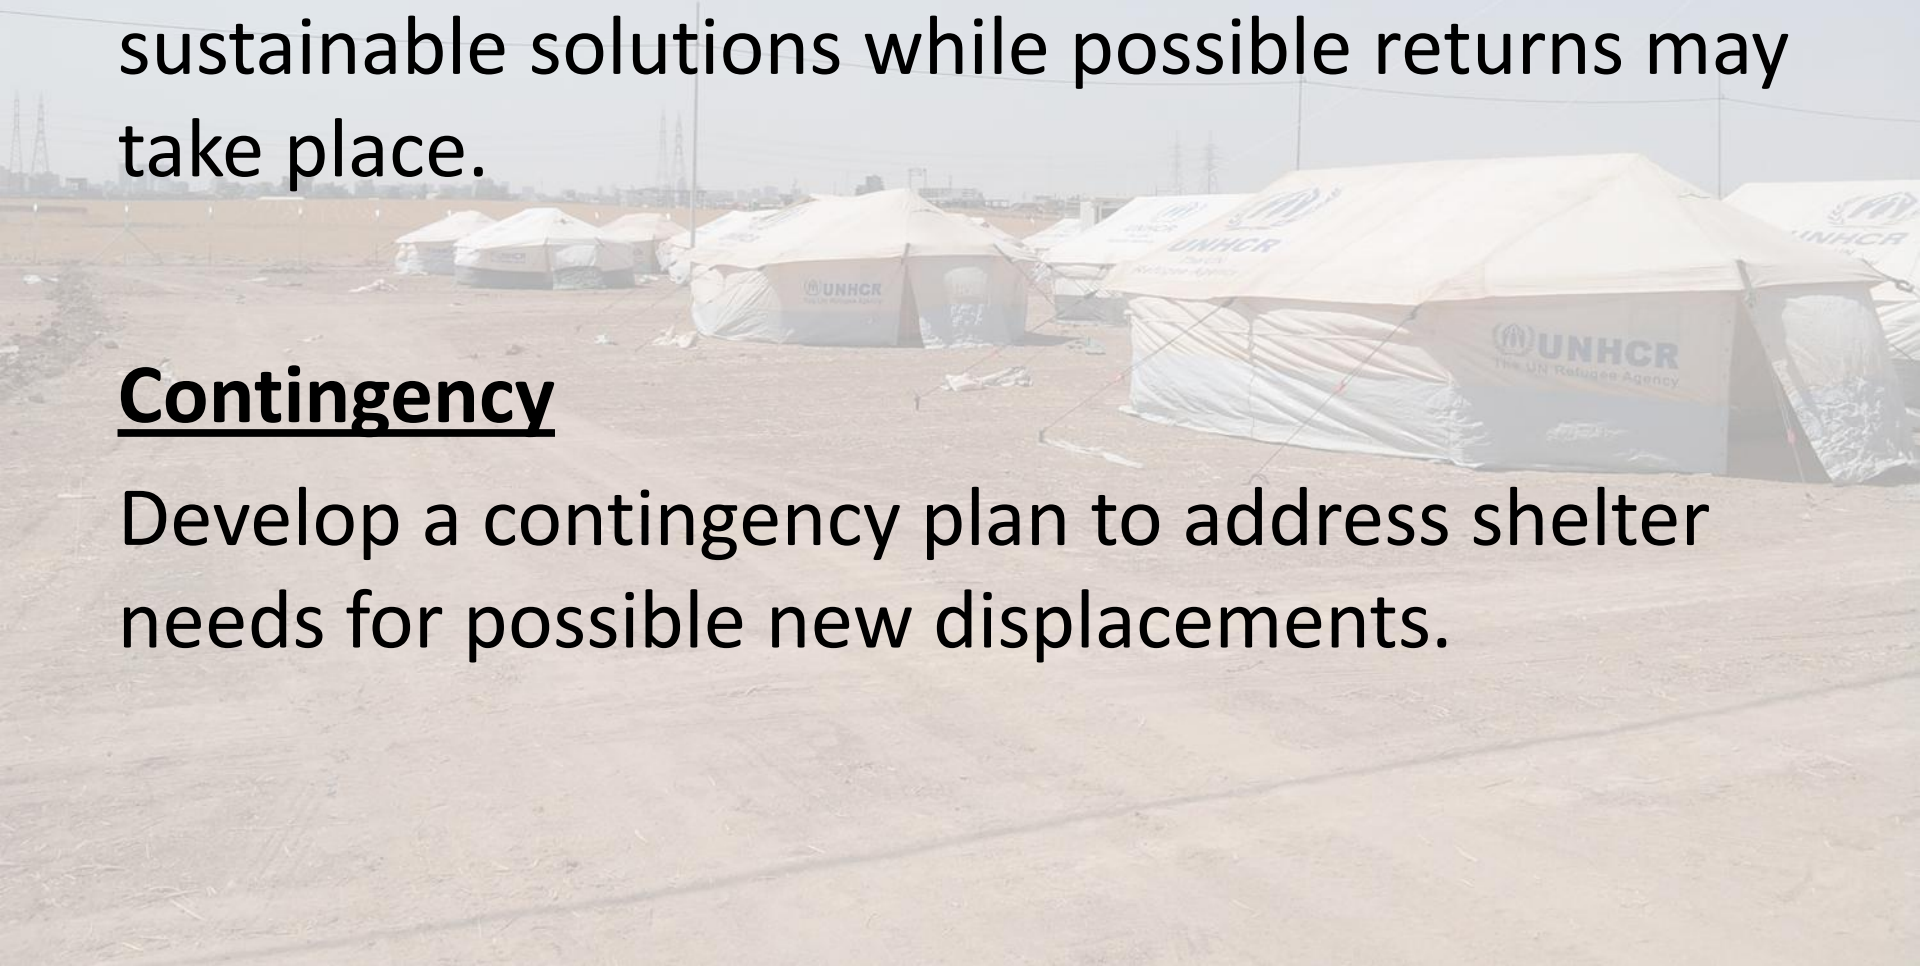

From Schools to Camps

- 129,000 IDPs living in 673 schools in Dohuk
- 7,000 IDPs living in 35 schools in Sulaymania
- 2,300 IDPs living in schools in Ainkawa (Erbil)

This means that **138,300 IDPs** need to be relocated from schools to camps


Develop a dedicated plan to vacate the schools including discussion with the Ministry of Education for the schools that may remain occupied.

Winterization

By November all elements of the plan need to be in place.

Winterization criteria need to be determined based on location, climate and type of shelter

Provision of subsidized Kerosene?

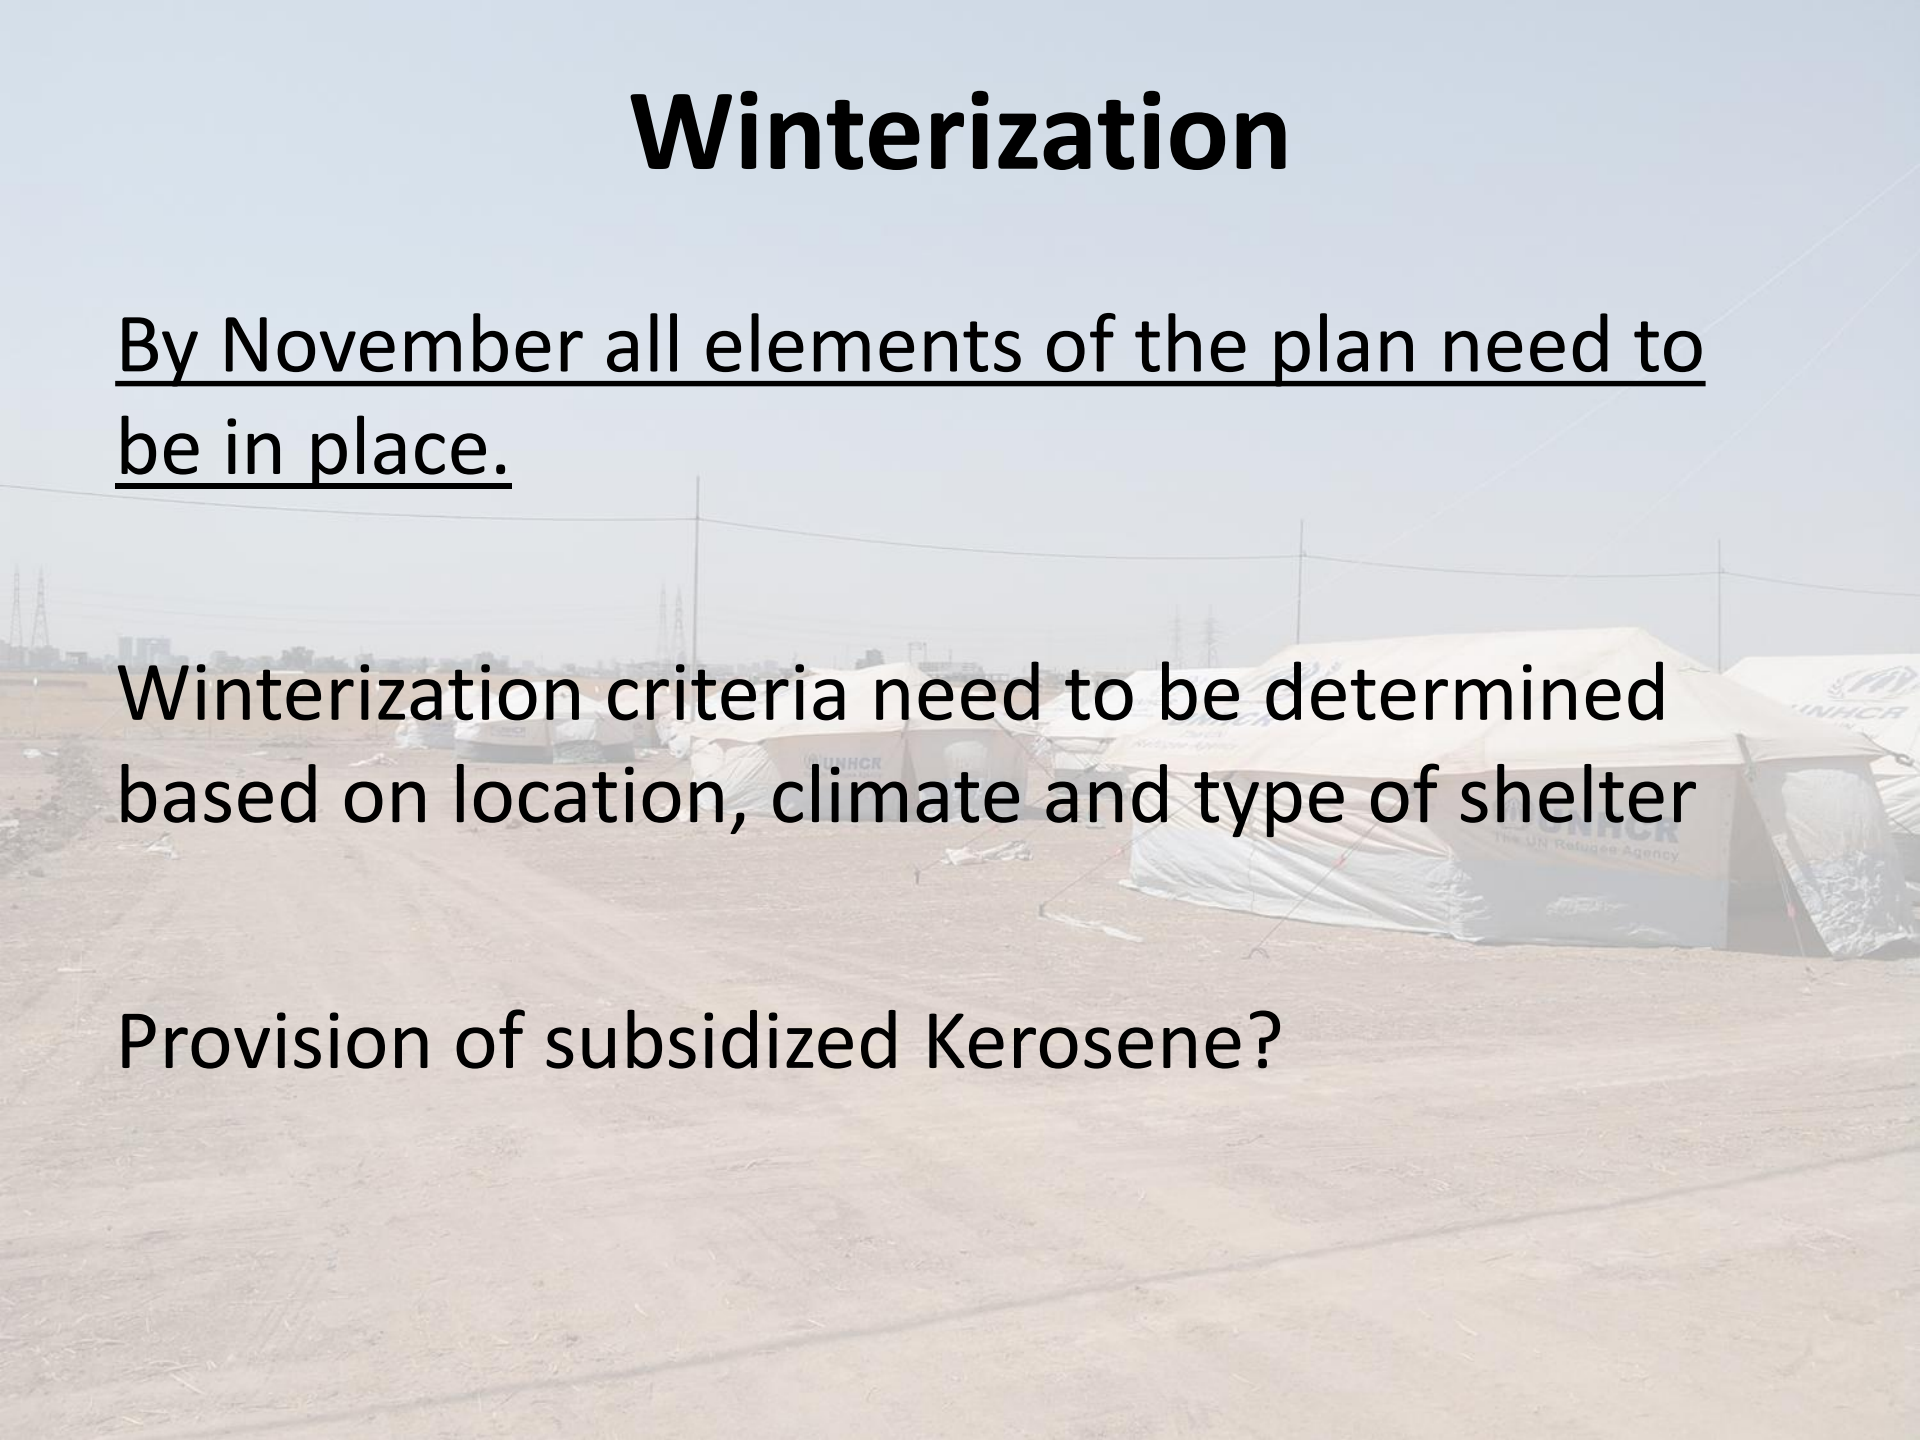


Planned camps

26 sites have been identified in the three Governorates

estimated total **absorption capacity** is equal to **240,000 individuals**

Potentially: 610,000 people remains in other locations (shared and rented accommodations)

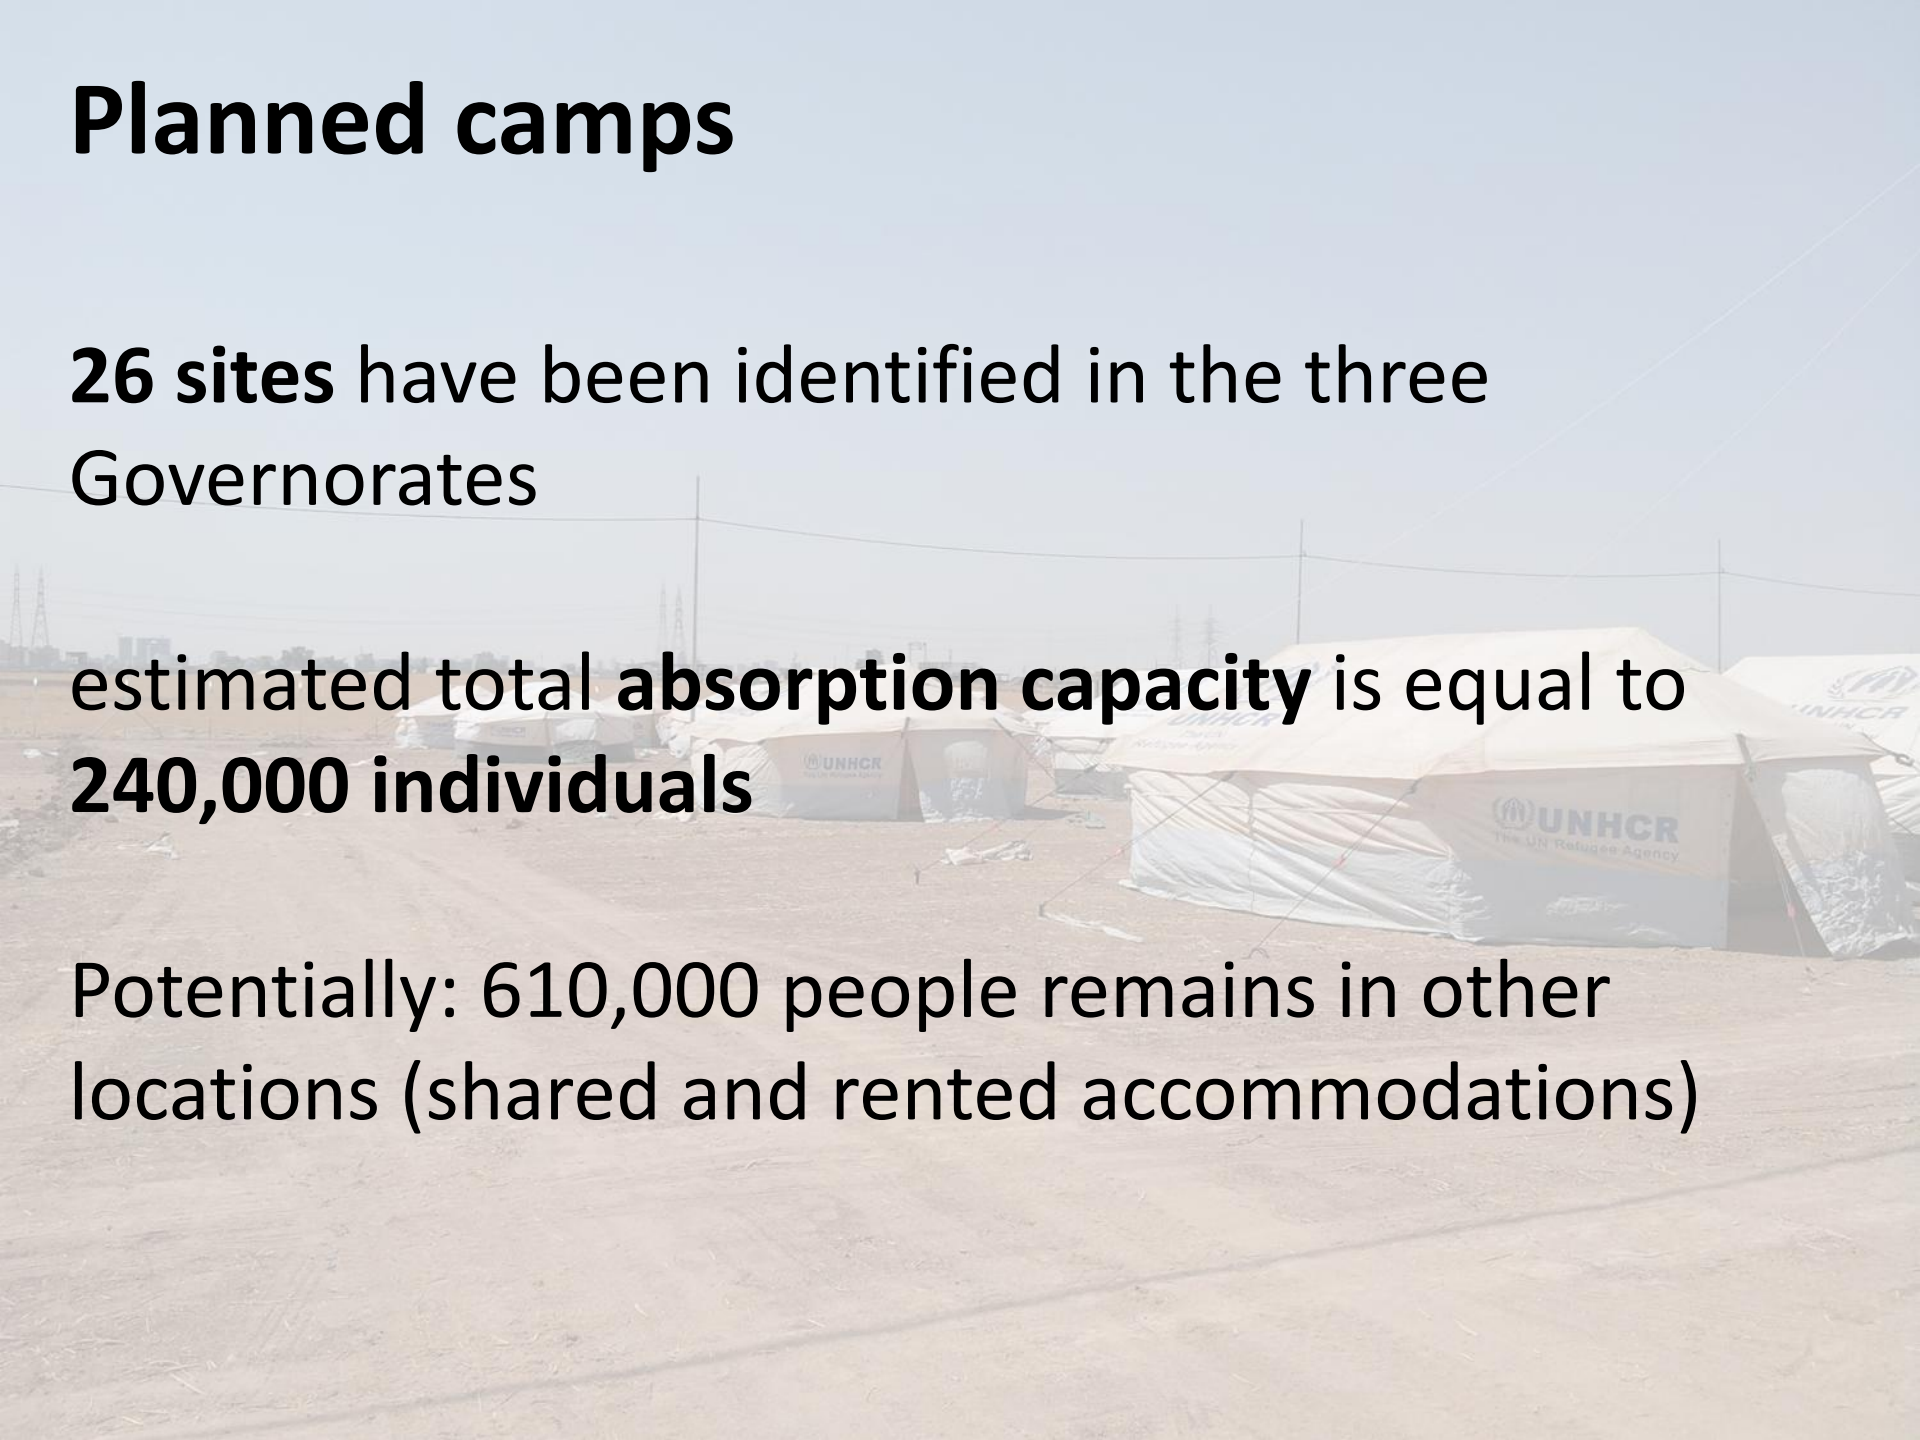

Erbil Governorate

Target population in schools/open is around **34,000** individuals

N	Location	IDP individuals	By who	Timeline
1	Baharka Old	3,300	UNHCR/UNICEF	completed
2	Baharka New	6,000	UNHCR/UNICEF	2 months
3	Ainkawa Municipality	4,000	UNHCR/UNICEF	2 months
4	Agriculture Land	1,800	UNHCR/UNICEF	10 days
5	Ainkawa MODM	1,500	MODM	TBC

sites absorption capacity **13,300** individuals

Erbil Governorate

Target population in schools/open is **around 34,000 individuals**

some **3,300 individuals** are already in camps

the population in need of shelter is equal to **30,700**

sites absorption capacity is **13,300 individuals**

Gap: 17,400 individuals

Estimated 2 months time to identify additional sites

Sulaimayia Governorate

Target population is estimated around **20,000 ind.**

N	Location	IDP individuals	By who	timeline
1	Mizafer, Chamchamal	6,000	UNHCR/UNICEF	2 months TBC
2	Qoratu, Kalar	6,000	UNHCR	2 months TBC
3	Arbat	6,000	UNHCR/UNICEF	3 weeks
4	Sitak	Around 2,400	??	??
5	Basijan	1,000	UN-Habitat	2 months (caravan)

Site absorption capacity **21,400 individuals**

Dohuk Governorate

Target population **200,000 individuals** TBC

N	Location	IDP ind	by who	Timeline
1	Bajet Kandala (new)	6,451	UNHCR/UNICEF	Two weeks
2	Bajet Kandala (old)	9,891	UNHCR/UNICEF	completed
3	Bersive I	15,000	AFAD	45 days ??
4	Bersive II	15,000	UNHCR/UNICEF	2 months
5	Agricultural Research I	21,500	MSB ??	??
6	Deraboun area	1,200	AFAD	completed
7	Sharya	17,000	AFAD	45 days
8	Khanke	8,000	UNHCR/UNICEF	1 months with slabs

Dohuk Governorate

N	Location	IDP ind	by who	timeline
9	Agricultural Research II	21,500	Baghdad??	??
10	Khanke extension	18,000	??	??
11	Garmawa	6,000	UNHCR/UNICEF	TBC by UNICEF Dohuk
12	Girshin	6,000	??	??
13	Bamarne I	6,000	UNDP/UN-Habitat	1.5 month Caravans)
14	Gabarto	24,000 confirmed	??	??
15	Khadia	20,000 ??	Dohuk Governorate (initial capacity of 6,000)	1 month including electricity
16	Aradan	6,000	??	??

Dohuk Governorate

Target population is around **200,000** individuals

Some **11,091 individuals** are already in camps

The population in need of shelter is **188,909 individuals**

Sites absorption capacity is **201,542 individuals**

Gap: 6 Sites for 97,000 individuals are not funded and no organisations identified/confirmed to implement

Challenges

- Financial, material and human resources
- Camp development timeline (**speed**)
- Financial implications: estimated cost **231 million USD**

